

I-680 Soundwall Project Construction Photos

Temporary Stock Pile Location for NB-14 Retaining Wall spoils at Vargas

All of the material from the stockpile has been moved and a new Vactor Pit as been installed per Caltrans request (part of the no-cost change order). The contractor still has to Hydroseed the area and install an access road to the pit for Maintenance.



NB-14A to be placed near Olive Drive

The installation of the Olive Trees completed today. Contractor to do one last major watering of the trees, then the city will become responsible for the trees.



Masonry Block

The contractor has completed installation of block at SB-2B, SB-5 and most of NB-8B. They are currently completing SB-1 and getting ready to go to SB-2A and SB-2B Extension.

Soundwall SB-1 (complete)



Soundwall SB-2A (block complete)



Soundwall SB-2B (complete)



Soundwall SB-2B Extension (block complete)



Soundwall NB-8B (in progress)



Soundwall NB-8B (in progress)




Soundwall SB-4A (in progress)



Soundwall SB-4B (in progress)



Soundwall SB-5 (complete)

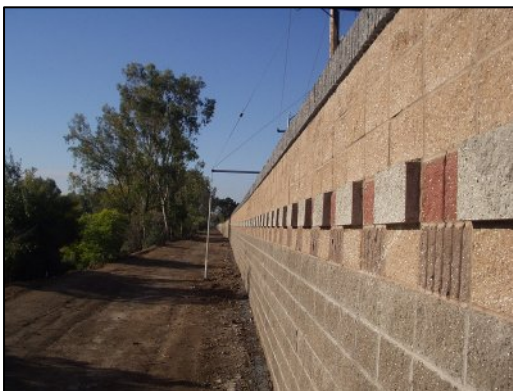

Soundwall SB-14A (in progress)



Soundwall SB-14B (in progress)



Retaining Walls

The contractor has completed all of the retaining wall on the project. NB-8A is ready for masonry block

Soundwall NB-8A (getting ready for block)

